ATD | CONSULTANTS

August 14, 2026

Mr. Jay Cordaro
Columbia Bank
19-01 Route 208 North
Fair Lawn, New Jersey

Re: JC Realty Ventures LLC
73 Broadway
Jersey City, New Jersey

Dear Mr. Cordaro,

In accordance with your request, ATD Consultants performed a site inspection at the above referenced project on August 11, 2026.

Based on our review of this project, ATD recommends that $98,203 for Application #3 (ATD #2), covering the period through August 5, 2026, be released for funding at this time.

If you have any questions or comments, please do not hesitate to call.

Sincerely,

Drew Jaime
Environmental & Construction Site Inspector
O: (973) 726-3518

73 BROADWAY

Jersey City, New Jersey

PROJECT DESCRIPTION

The project consists of the construction of a new triplex-style residence and the associated site work, located at 73 Broadway, Jersey City, New Jersey.

WORK COMPLETED

Application #3 (ATD #2), dated August 5, 2026

			Requested		Approved
1	Dumpsters	$	3,000	$	1,500
2	Irrigation / Sprinklers*		6,500		3,250
3	Roofing		45,000		30,000
4	Rough Electrical		32,000		32,000
5	Builder / GC Fee (15%)		50,000		50,000
	TOTAL:	$	136,500	$	116,750

COMMENTS

The items listed above are 100% complete, except for the following:

1. Dumpsters - Amount requested is adjusted to more accurately reflect the overall percent complete of the project. Contractor is requesting 68% of this line item.
2. Irrigation / Sprinklers* - Amount requested is adjusted to reflect work complete of 50%. Contractor is requesting 100% of this line item. Work remaining is the installation of the riser, controls and the sprinkler heads.
3. Roofing - Amount requested is adjusted to reflect work complete of 67%. Contractor is requesting 100% of this line item. Work remaining is the

installation of the membrane on the parapet walls, and the installation of the copings.

4. Builder / GC Fee (15%) - Amount requested approved. Contractor is requesting 45% of this line item, which is acceptable.

WORKMANSHIP

The quality of workmanship is acceptable; however, the plans were not reviewed. There was some trade activity (carpenters, electricians) at the time of our site inspection.

PROGRESS

The Project is approximately 42% complete, representing an increase of 13% since the last site inspection was performed. This progress represents an average of 6% per month since ATD's last site inspection on June 4, 2026.

FUNDING

Application #3 (ATD #2), dated August 5, 2026

		Requested		Approved
Original Contract Sum	$	1,019,220	$	891,650
Net Change by Change Orders		0		0
Contract Sum to Date	$	1,019,220	$	891,650
Total Completed and Stored to Date	$	461,900	$	375,950
Total Retainage to Date**		46,190		0
Total Earned Less Retainage		415,710		375,950
Less Previous Certificates of Payment		292,860		259,200
Current Payment Due	*$*	*122,850*	*$*	*116,750*

(not final payment recommended by ATD)

ATD Funding Recommendation

Current Payment Due	$	116,750
Percent Funding this Draw***		84.11%

Final Funding Recommended by ATD	***$***	***98,203***

**It should be noted that the Irrigation / Sprinkler line item applies to the Fire Sprinkler System, and there will not be an irrigation system installed.*

***Please note that while retainage is being shown on the Borrower's AIA, it is ATD's understanding that Columbia Bank is not holding retainage on this loan.*

****Columbia Bank has agreed to fund $750,000 towards the total construction and site costs of $891,650. Therefore, funding will be calculated at 84.11%.*

ACKNOWLEDGEMENT

This Construction Progress Report is expressly and exclusively for the sole use and benefit of the Client and is not for the use or benefit of, nor may it be relied upon by, any other person or entity. ATD Consultants shall have no responsibility to the Borrower, Architect, Engineer(s), Contractor(s), and others retained by the Borrower nor shall ATD Consultants have any liability for the acts or omissions of any of the aforementioned, their agents, or employees. The contents of this report may not be quoted in whole, in part, or distributed to any person or entity other than the Financial Institution hereof or its successors, assigns, or participants without, in each case, the advance written consent of ATD Consultants.

ATD's Construction Progress Report represents the progress of the project at the time of ATD's site inspection and the general compliance with the drawings and specifications reviewed. It should be noted the many of the components installed may not be observable at the time of the inspection (footings, framing, rough mechanicals). This report is only a recommendation to the financial institution to release funding to the borrower and not a recommendation for the borrower to release funds to the contractor. ATD Consultants' services reflect our best judgment and observations in accordance with generally accepted construction-consulting practices, at the time our service is rendered, but ATD Consultants is not providing warranties or guarantees on any aspect or component of the Project.

ATD Consultants is not a guarantor or insurer of the adequacy and sufficiency of the Construction Documents or Budget to complete the Project. The review does not verify the adequacy of the underlying computations, critical assumptions, and final interpretations as they relate to the design of the Project. Additionally, the accuracy of dimensions, quantities, sizes, and capacities shown as required for any site or building component is not a part of this evaluation. Such determination and verification is considered to be the responsibility of the Architects, Engineers and Specialized Consultants of Record, as would be determined to be adequate as provided for in their proposals to the property developer.

ATD Consultants' role is limited to the specific services described herein which are not intended to take the place of on-site construction management, or the Architect, or Engineer(s), of Record's design and construction administrative duties. Factual information regarding existing site conditions and designed solutions provided by the Client or their representatives has been assumed to be correct, complete, and approved by the respective governing authorities. The conclusions presented are based on the information provided to us for review. This document review encompasses only the facilities and site work as identified in the information provided to ATD Consultants.

Columbia Bank
Construction Inspection Report

Borrower's Entity: JC Realty Ventures LLC
Project Address: 73 Broadway
Jersey City, New Jersey

Contact Name: Kunal Shah
Contact Phone: 2014011296
Contact Email: kunalshah0323@gmail.com

Loan Amount: $750,000
Inspector: ATD Consultants

Item #	Item	Scheduled Value	Draw 1	Draw 2	Draw 3	Draw 4	Draw 5	Draw 6	Draw 7	Draw 8	Draw 9	Draw 10	Total Completed	Balance to Finish	% Total Completed
			6/4/26	8/11/26											
1	**Architect Fees**	0	0										0	0	0%
2	**Engineer Fees**	0	0										0	0	0%
3	**Surveyor Fees**	0	0										0	0	0%
4	**Testing Fees**	0	0										0	0	0%
5	**Permits**	0	0										0	0	0%
6	Temporary Utilities	4,500	4,500										4,500	0	100%
7	Site Clearing	2,000	2,000										2,000	0	100%
8	Grading/Excavation/Dumpsters	15,000	15,000										15,000	0	100%
9	Dumpsters	8,000	2,400	1,500									3,900	4,100	49%
10	Security Fencing	2,500	2,500										2,500	0	100%
11	Concrete Walls/Foundation	45,000	45,000										45,000	0	100%
12	Foundation Waterproofing	4,000	4,000										4,000	0	100%
13	Concrete Slabs	10,000	10,000										10,000	0	100%
14	Concrete Driveway	5,000	0										0	5,000	0%
15	Concrete Walks	3,500											0	3,500	0%
16	Roof Deck	12,000											0	12,000	0%
17	Water / Sewer Connections	12,300	12,300										12,300	0	100%
18	Irrigation / Sprinklers	6,500		3,250									3,250	3,250	50%
19	Fencing	2,500	2,500										2,500	0	100%
20	Equipment Rental	2,500	2,500										2,500	0	100%
21	Framing	120,000	120,000										120,000	0	100%
22	Structural Steel	6,000	6,000										6,000	0	100%
23	Subfloors	5,000	5,000										5,000	0	100%
24	Roofing	45,000		30,000									30,000	15,000	67%
25	Sheathing	12,000	12,000										12,000	0	100%
26	Exterior Finish	45,000											0	45,000	0%
27	Soffit / Fascia	4,500											0	4,500	0%
28	Gutters / Downspouts	7,000											0	7,000	0%
29	Windows / Skylights	35,000											0	35,000	0%
30	Exterior Doors	3,000											0	3,000	0%
31	Entry Door	5,500											0	5,500	0%
32	Exterior Painting	2,500											0	2,500	0%
33	Exterior Stairs / Railings	7,000											0	7,000	0%
34	Garage Doors	2,500											0	2,500	0%
35	Rough Plumbing	27,000	13,500										13,500	13,500	50%
36	Finish Plumbing	5,000											0	5,000	0%
37	Plumbing Fixtures	1,800											0	1,800	0%
38	Water Heater(s)	8,000											0	8,000	0%
39	Rough Electrical	32,000		32,000									32,000	0	100%
40	Finish Electrical	5,000											0	5,000	0%
41	Fixtures Electrical	1,800											0	1,800	0%
42	HVAC Rough	24,000											0	24,000	0%
43	HVAC Finish (Furnace, Condenser)	8,000											0	8,000	0%
44	Fire Protection	3,500											0	3,500	0%
45	Insulation	16,000											0	16,000	0%
46	Interior Walls & Ceilings (Drywall/Plaster)	26,000											0	26,000	0%
47	Interior Paint	10,000											0	10,000	0%
48	Kitchen Cabinets	40,000											0	40,000	0%
49	Kitchen Countertops	25,000											0	25,000	0%
50	Appliances	18,000											0	18,000	0%
51	Bath Vanities	14,000											0	14,000	0%
52	Hardware and Mirrors	3,500											0	3,500	0%
53	Wall Tile / Shower Surround	12,000											0	12,000	0%
54	Shower Pans / Tub Set	2,200											0	2,200	0%
55	Tile Floors	7,500											0	7,500	0%
56	Hardwood Floors	25,000											0	25,000	0%
57	Interior Doors	11,000											0	11,000	0%
58	Door Trim	7,000											0	7,000	0%
59	Interior Trim	2,000											0	2,000	0%
60	Shower Doors	7,500											0	7,500	0%
61	Final Clean-up	1,500											0	1,500	0%
62	Builder / GC Fee (15%)	112,050		50,000									50,000	62,050	45%

Columbia Bank
Construction Inspection Report

Borrower's Entity: JC Realty Ventures LLC
Project Address: 73 Broadway
Jersey City, New Jersey

Contact Name: Kunal Shah
Contact Phone: 2014011296
Contact Email: kunalshah0323@gmail.com

Loan Amount: $750,000
Inspector: ATD Consultants


Item #	Item	Scheduled Value	Draw 1	Draw 2	Draw 3	Draw 4	Draw 5	Draw 6	Draw 7	Draw 8	Draw 9	Draw 10	Total Completed	Balance to Finish	% Total Completed
			6/4/26	8/11/26											
63	Contingency (10%)	0											0	0	0%
	Total This Inspection	891,650	259,200	116,750									375,950	515,700	42%
	Previously Completed		0	259,200											
	Total Completed to Date		259,200	375,950											
	Percent Funding		84.11%	84.11%											
	Percent Funding Amount this Draw		218,023	98,203											
	Total Percent Funding to Date		218,023	316,226											

OK to Fund $98,203

ATD Consultants 8/11/26



FRONT ELEVATION

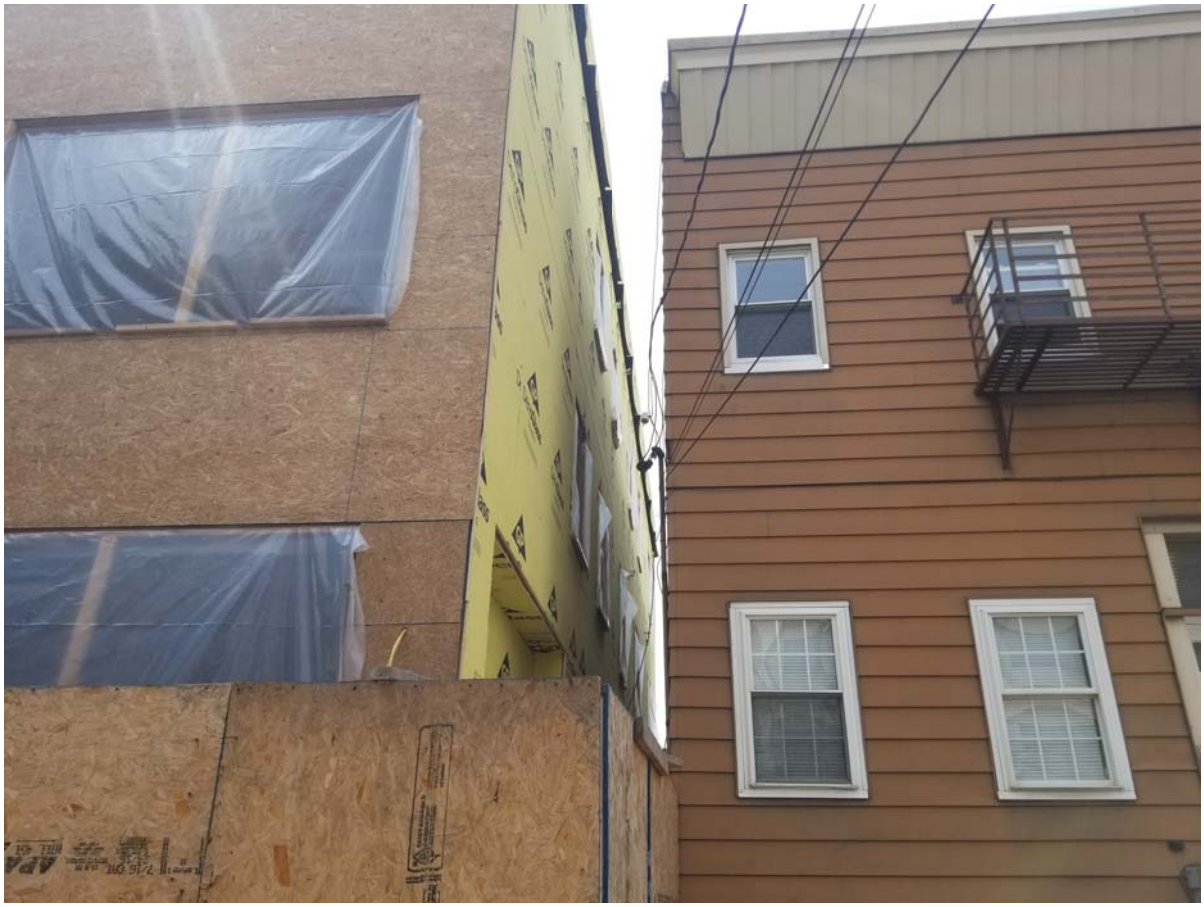

RIGHT ELEVATION



LEFT ELEVATION



REAR ELEVATION



REAR ELEVATION



1ST FLOOR



2ND FLOOR



3RD FLOOR



TYPICAL BATHROOM




TYPICAL BATHROOM



TYPICAL UTILITY CLOSET



TYPICAL MECHANICAL CLOSET

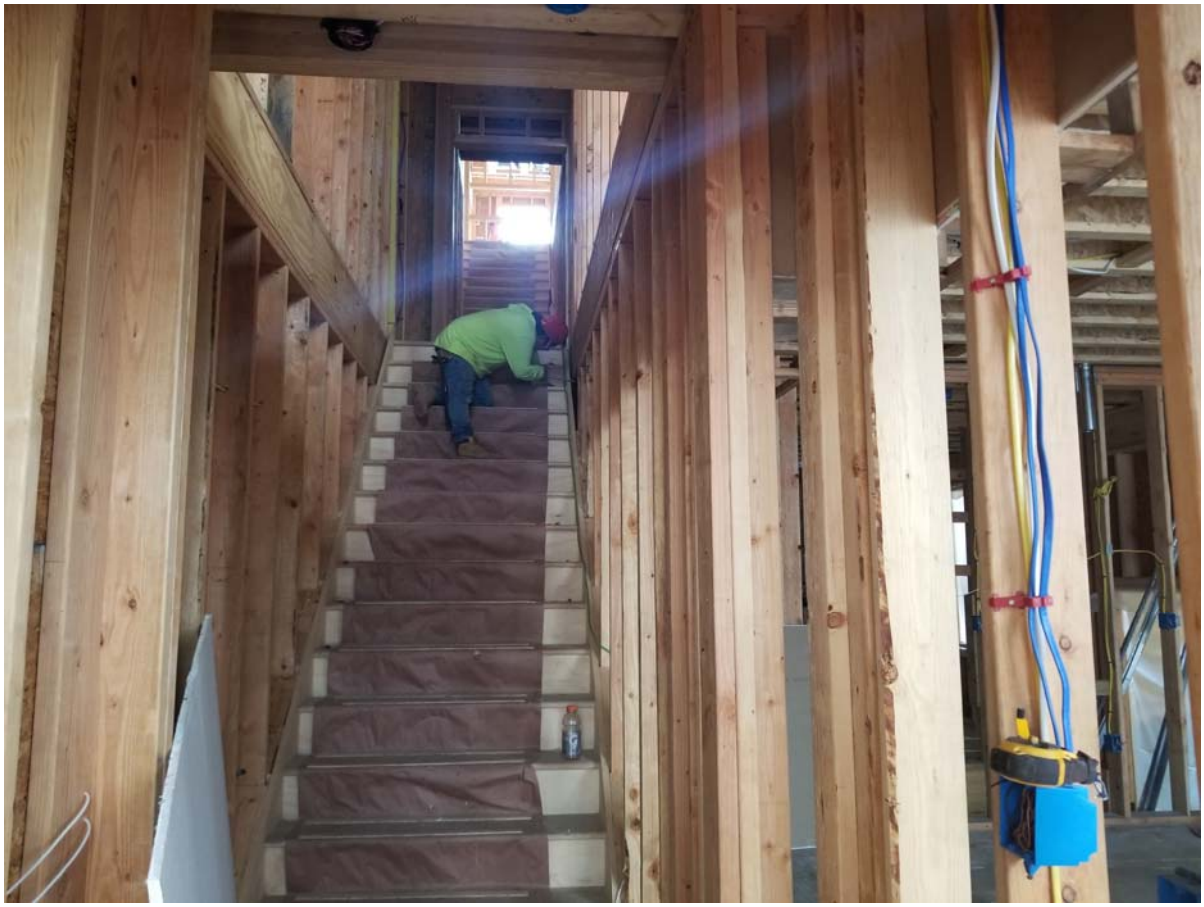

STAIRWELL



STAIRWELL



BALCONY



ROOF



ROOF




REAR ADDITION



ADDITION 1ST FLOOR



ADDITION 2ND FLOOR

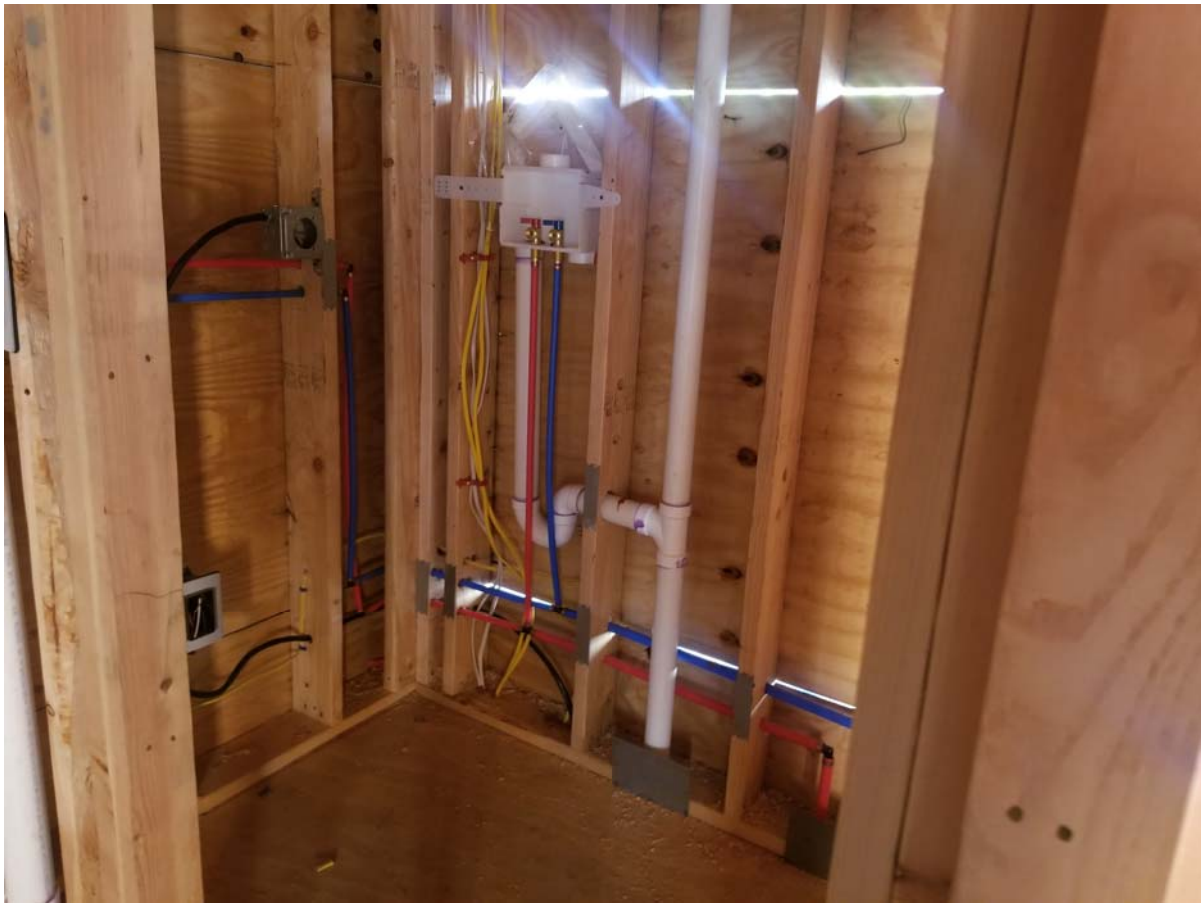

ADDITION LAUNDRY CLOSET



ADDITION BATHROOM



BULKHEAD



BULKHEAD



UNDERGROUND ELECTRIC



UNDERGROUND ELECTRIC



MECHANICAL ROOM
